

#### City of Doral Parks Bond Program Quarterly Update to City Council

















Quarter 1&2 2025





# **Projects Completed**











**Doral White Course Park** 









Project Level Schedule









	Doral Meadow Park	Doral White Course Park	Morgan Levy Park	Trails and Tails Park		
Begin Procurement Process	Nov 2019	Sep 2019	Nov 2019	Dec 2019		
Notice to Proceed Design	Jan 2020	Mar 2020	Sep 2020	Dec 2020		
Notice to Proceed Construction	Jul 2020	Apr 2021	Aug 2020	Aug 2021		
Substantial Completion	Jun 2021	May 2022	Mar 2021	Jun 2022		
Closeout	Aug 2021	Jul 2022	May 2021	Jul 2022		





Project Level Schedule









	Doral Cultural Arts Center	Doral Central Park Phase IV	Trails Network Phase I Trails	Trails Network Phase II Lighting		
Begin Procurement Process	Jul 2019	Feb 2020	Apr 2020	Jul 2023		
Notice to Proceed Design	Sep 2019	Apr 2020	May 2021	Jul 2023		
Notice to Proceed Construction	Mar 2021	Mar 2021	Jul 2021	May 2025 (Greenway)		
Substantial Completion	Oct 2022	May 2025	Feb 2022	TBD		
Closeout	Feb 2024	Sept 2025	Apr 2023	TBD		





#### DORAL

#### **DORAL PARKS BOND BUDGET SUMMARY**


June 2025	Α	В	С		D	E	
Projects	Original Program Budgets (NOV 2019)	Budgeted Sub-Total	Expended to Date	Encumbered		Available (B-C-D)	
Doral Central Park	\$ 119,000,000.00	\$ 167,956,872.53	\$ 158,570,616.35	\$	4,326,157.44	\$ 5,060,098.74	
Doral Cultural Arts Center	\$ 9,800,000.00	\$ 10,890,911.97	\$ 10,859,546.51	\$	(0.00)	\$ 31,365.46	
Doral White Course Park	\$ 4,100,000.00	\$ 4,024,273.12	\$ 3,975,871.07	\$	6,600.00	\$ 41,802.05	
Morgan Levy Park	\$ 143,000.00	\$ 701,439.03	\$ 704,037.55	\$	-	\$ (2,598.52)	
Trails and Tails Park	\$ 926,000.00	\$ 996,140.65	\$ 956,857.33	\$	5,910.51	\$ 33,372.81	
Doral Pedestrian Bridge (Canceled)	\$ 3,500,000.00	\$ 160,633.80	\$ 160,633.80	\$	-	\$ -	
Trails Network	\$ 3,900,000.00	\$ 2,336,495.92	\$ 560,625.04	\$	26,559.85	\$ 1,749,311.03	
Doral Meadow Park	\$ 1,500,000.00	\$ 1,737,184.70	\$ 1,652,890.96	\$	0.00	\$ 84,293.74	
Administrative Cost	\$ 6,900,000.00	\$ 8,078,040.95	\$ 7,512,718.59	\$	0.00	\$ 565,322.36	
Potential Savings	\$ -	\$ 2,806,976.33	\$ -	\$	-	\$ 2,806,976.33	
	Original Program Budgets (NOV 2019)	Budgeted Sub-Total	Expended to Date		Encumbered	Available (B-C-D)	
TOTALS:	\$ 149,769,000.00	\$ 199,688,969.00	\$ 184,953,797.20	\$	4,365,227.80	\$ 10,369,944.00	





#### **Program Budget Report**

**Budget Total** \$199,688,969.00

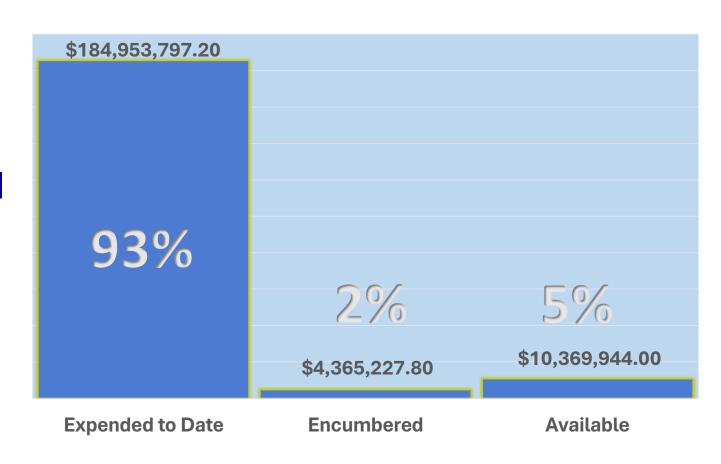







Skate Park & Kayak Area





Boardwalk & Volleyball Courts





Amphitheater





Multipurpose Field





Aquatics, Outdoors Basketball Courts and Tennis Courts





Community Center and Parking Lot














Phase I
Site & Underground Infrastructure Q1&2 2025











Phase IV
Aquatics Center - Construction Q1&2 2025










Phase IV
Community Center - Construction Exterior
Q1&2 2025











Phase IV
Community Center - Construction Interior Q1&2 2025









Phase IV

Doral Central Park Opening – May 17<sup>th</sup>, 2025















Phase IV

Doral Central Park Opening – May 17<sup>th</sup>, 2025

















- Phase I
  - Closeout.
- Phase II and III:
  - Closeout.
- Phase IV:

#### **Community Center**

• Closeout.

#### Aquatics

Closeout.















