ID	Task Name	Duration	Start
1	***City of Doral CCTV & Access Control Installation***	**111 days**	**Wed 5/1/24**
2	*Award of Contract*	1 day	Wed 5/1/24
3	***Part-1 Phase 2 & 3***	**25 days**	**Thu 5/2/24**
4	*Design & Administrative*	2 days	Thu 5/2/24
5	*Submit Submittals and Shop Drawings to the Customer for approvals*	1 day	Mon 5/6/24
6	*Customer Approved Submittals & Shop Drawings*	1 day	Tue 5/7/24
7	*Submit for permits*	1 day	Wed 5/8/24
8	***Approved Permits by the AHJ's***	**0 days**	**Wed 5/8/24**
9	*Pending Approvals from AHJ*	10 days	Wed 5/8/24
10	*Order/ Receive Equipment*	10 days	Wed 5/8/24
11	***CCTV Installation***	**14 days**	**Thu 5/9/24**
12	*Mobilization*	1 day	Thu 5/9/24
13	*Survey Existing Head-End (IP Addr)*	2 days	Thu 5/9/24
14	***Outdoor Pole Cameras (40)***	**8 days**	**Mon 5/13/24**
15	*Cable Installation*	5 days	Mon 5/13/24
16	*Camera Installation*	3 days	Mon 5/20/24
17	***Indoor & Outdoor cameras (2)***	**1 day**	**Thu 5/23/24**
18	*Cable Installation*	1 day	Thu 5/23/24
19	*Camera Installation*	1 day	Thu 5/23/24
20	*Electrical Rough Inspection*	1 day	Thu 5/23/24
21	*Programming*	2 days	Thu 5/23/24
22	*Commissioning*	2 days	Mon 5/27/24
23	***Access Control Installation***	**4 days**	**Thu 5/23/24**
24	*Mobilization*	1 day	Thu 5/23/24
25	*Install Head End*	1 day	Fri 5/24/24
26	***Biometrics CR/Door (2)***	**2 days**	**Mon 5/27/24**
27	*Cable Installation*	1 day	Mon 5/27/24
28	*Device Installation*	1 day	Tue 5/28/24
29	*Electrical Rough Inspection*	1 day	Tue 5/28/24
30	***Testing / Approvals***	**5 days**	**Wed 5/29/24**
31	*Final Contractor Testing*	2 days	Wed 5/29/24
32	*Final Contractor Punch List*	1 day	Fri 5/31/24
33	*Testing with the AHJ*	1 day	Mon 6/3/24
34	*Final Owner Sign Off*	1 day	Tue 6/4/24
35	***Close Out***	**4 days**	**Fri 5/31/24**
36	*As Built Drawings*	1 day	Fri 5/31/24
37	*O&M Manuals*	1 day	Tue 6/4/24

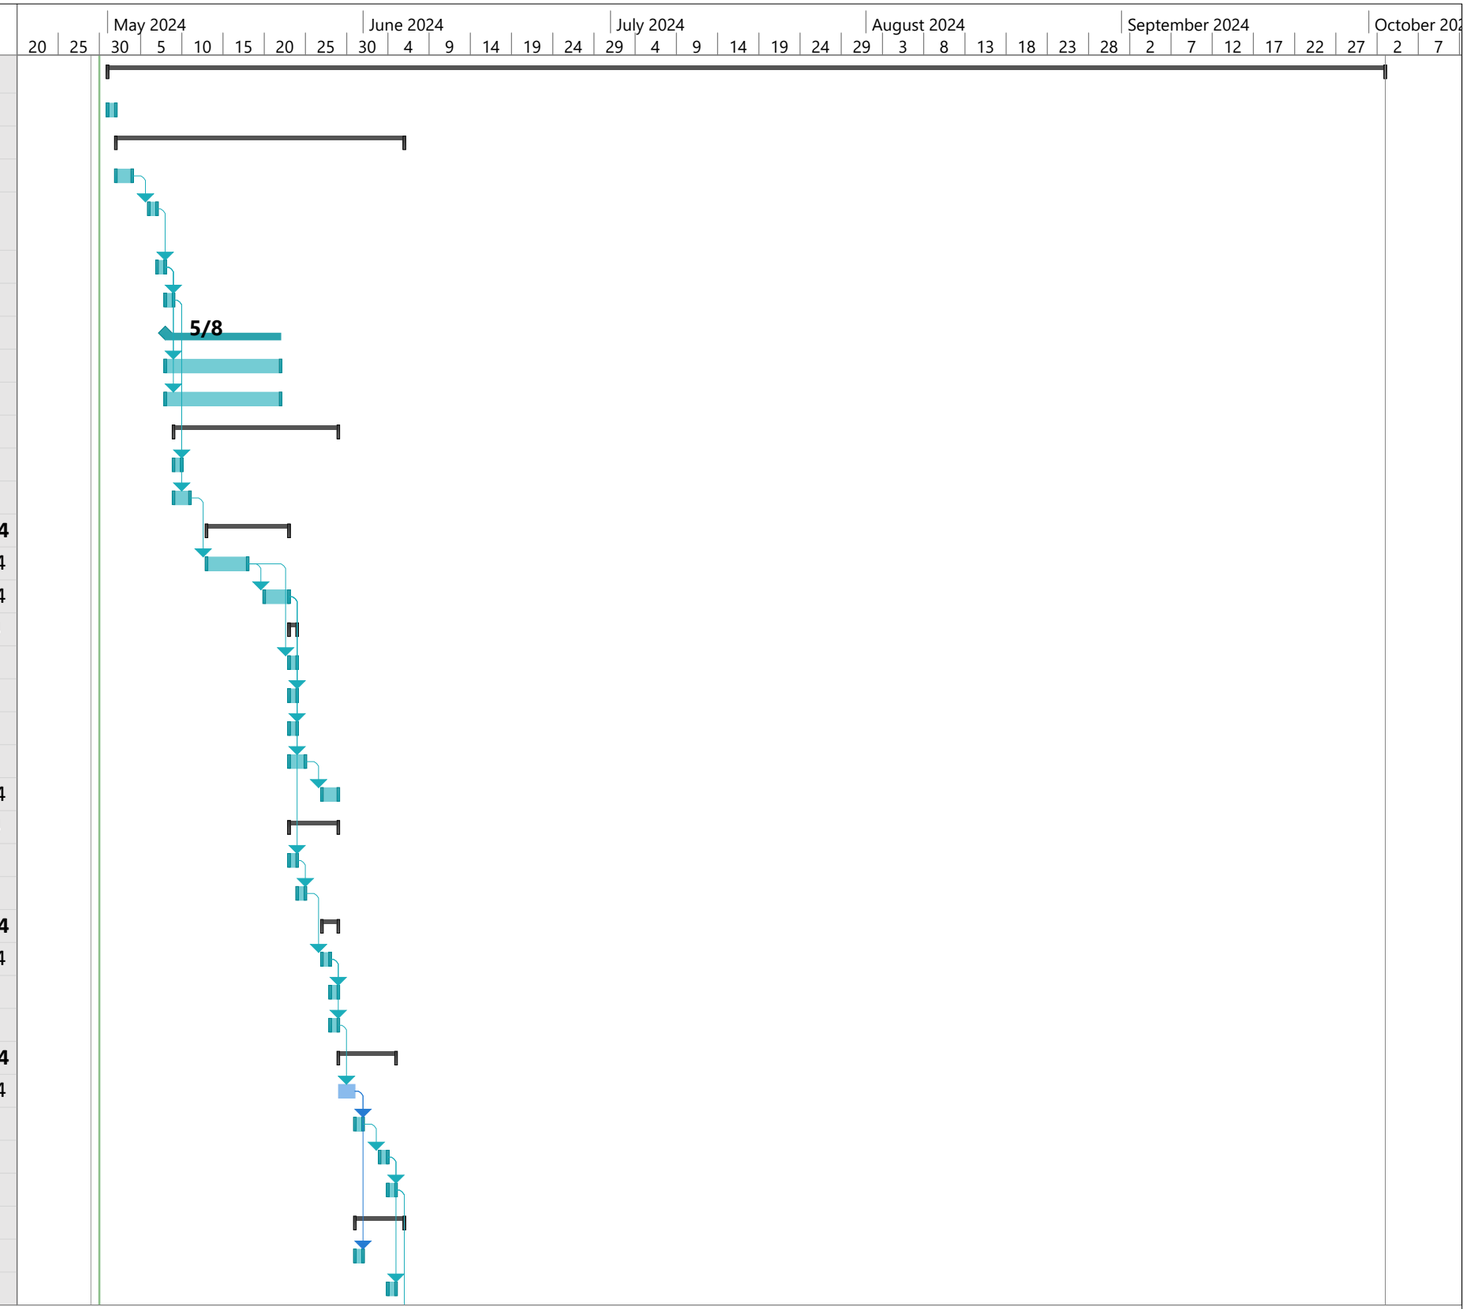

Project: City Of Doral CCTV & A
Date: Tue 4/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start
38	*Misc Close Out Submittals*	1 day	Wed 6/5/24
39	*Training*	1 day	Wed 6/5/24
40	***Part-2 (A) Phase-4 (REC CENTER)***	**53 days**	**Tue 5/7/24**
41	*Design & Administrative*	5 days	Tue 5/7/24
42	*Submit Submittals and Shop Drawings to the Customer for approvals*	1 day	Tue 5/14/24
43	*Customer Approved Submittals & Shop Drawings*	3 days	Wed 5/15/24
44	*Submit for permits*	1 day	Mon 5/20/24
45	***Approved Permits by the AHJ's***	**0 days**	**Tue 5/21/24**
46	*Pending Approvals from AHJ*	10 days	Tue 5/21/24
47	*Order/ Receive Equipment*	15 days	Tue 5/21/24
48	***CCTV Installation***	**32 days**	**Tue 6/4/24**
49	*Mobilization*	1 day	Tue 6/4/24
50	*Survey Existing Head-End (IP Addr)*	3 days	Tue 6/4/24
51	***Outdoor Pole Cameras (6)***	**2 days**	**Fri 6/7/24**
52	*Cable Installation*	1 day	Fri 6/7/24
53	*Camera Installation*	1 day	Mon 6/10/24
54	***Indoor & Outdoor cameras (57)***	**25 days**	**Tue 6/11/24**
55	*Cable Installation*	15 days	Tue 6/11/24
56	*Camera Installation*	10 days	Tue 7/2/24
57	*Inspections*	2 days	Tue 7/2/24
58	*Programming*	5 days	Tue 7/2/24
59	*Commissioning*	2 days	Tue 7/16/24
60	***Access Control Installation***	**26 days**	**Tue 6/4/24**
61	*Mobilization*	1 day	Tue 6/4/24
62	*Install Head End*	5 days	Tue 6/4/24
63	***Regular CR/Door (19)***	**8 days**	**Tue 6/11/24**
64	*Cable Installation*	5 days	Tue 6/11/24
65	*Device Installation*	3 days	Tue 6/18/24
66	***Biometrics CR/Door (6)***	**6 days**	**Fri 6/21/24**
67	*Cable Installation*	4 days	Fri 6/21/24
68	*Device Installation*	2 days	Thu 6/27/24
69	***DC/DS Door (22)***	**5 days**	**Mon 7/1/24**
70	*Cable Installation*	3 days	Mon 7/1/24
71	*Device Installation*	2 days	Thu 7/4/24
72	*Inspections*	2 days	Mon 7/1/24
73	*Programming*	3 days	Tue 6/18/24
74	*Commisioning*	2 days	Mon 7/8/24

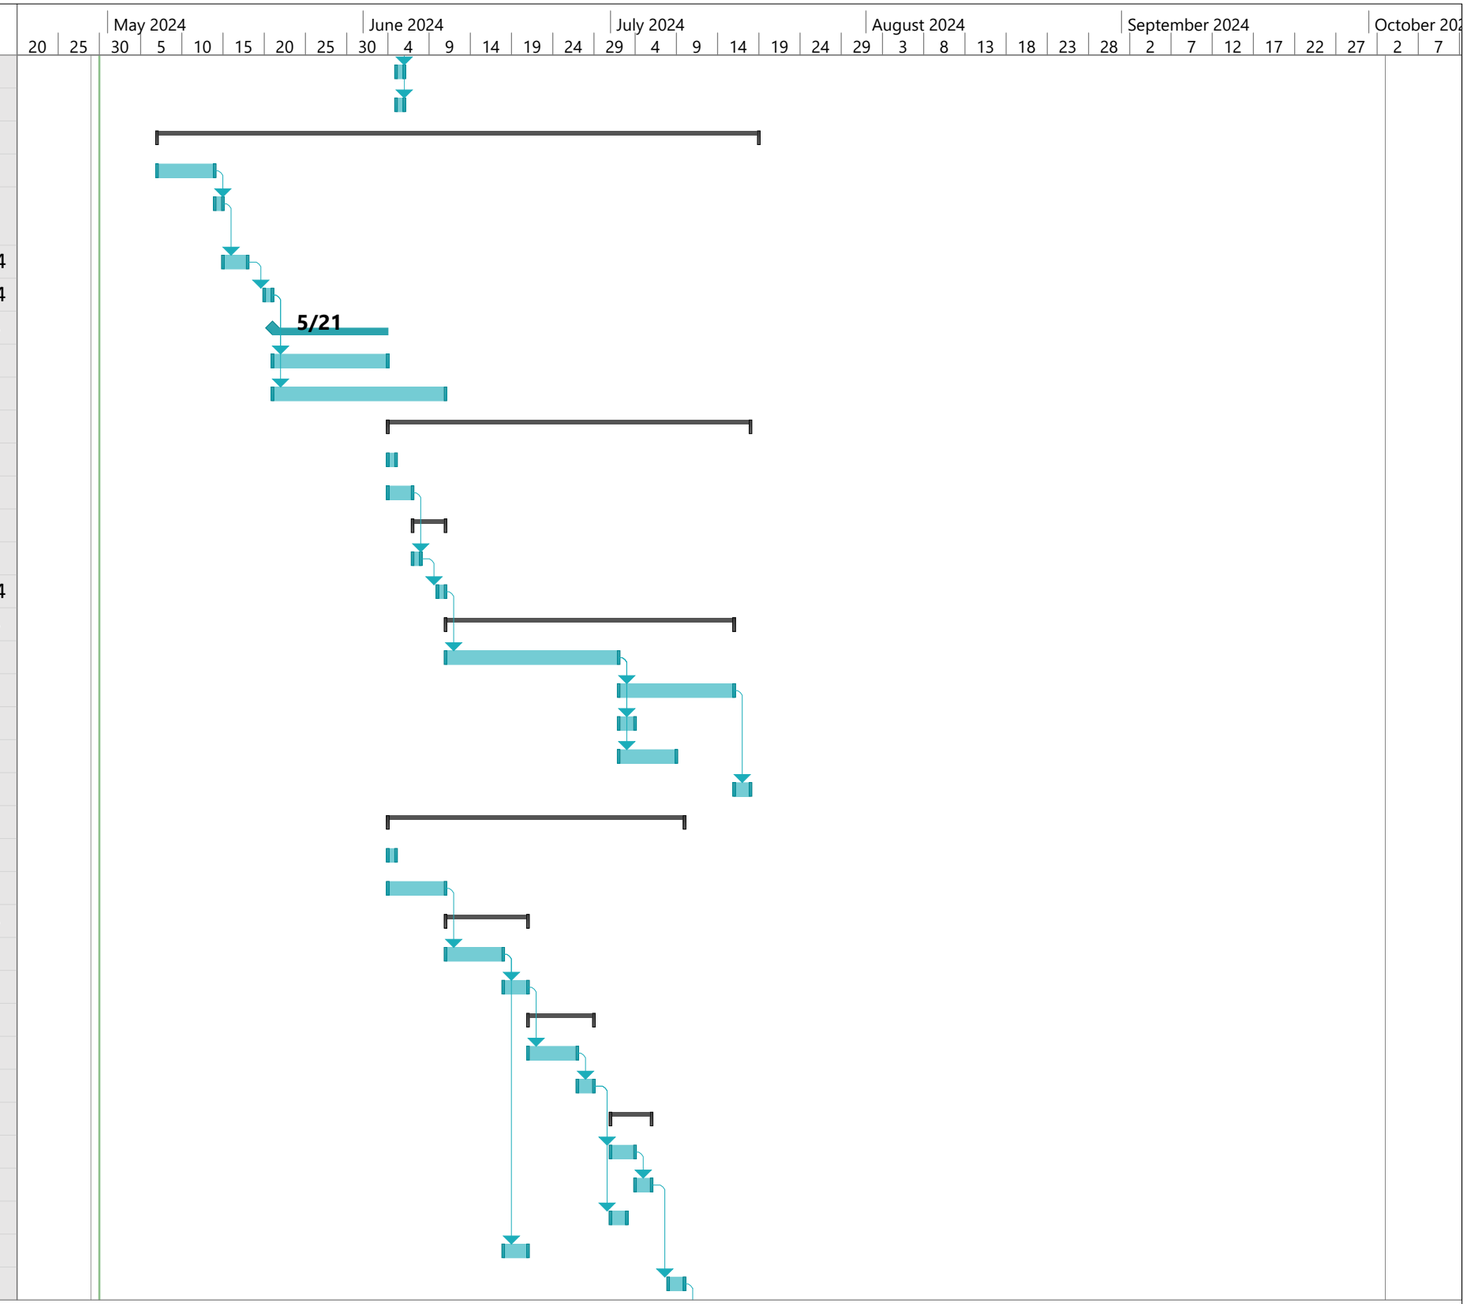

Project: City Of Doral CCTV & A
Date: Tue 4/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start
75	***Testing / Approvals***	**7 days**	**Wed 7/10/24**
76	*Final Contractor Testing*	2 days	Wed 7/10/24
77	*Final Contractor Punch List*	2 days	Fri 7/12/24
78	*Testing with the AHJ*	2 days	Tue 7/16/24
79	*Final Owner Sign Off*	1 day	Thu 7/18/24
80	***Close Out***	**3 days**	**Tue 7/16/24**
81	*As Built Drawings*	1 day	Tue 7/16/24
82	*O&M Manuals*	1 day	Wed 7/17/24
83	*Misc Close Out Submittals*	1 day	Wed 7/17/24
84	*Training*	1 day	Thu 7/18/24
85	***Part-2 (B) Phase-4 (AQUATIC CENTER)***	**43 days**	**Mon 8/5/24**
86	***CCTV Installation***	**14 days**	**Mon 8/5/24**
87	*Mobilization*	1 day	Mon 8/5/24
88	*Survey Existing Head-End (IP Addr)*	2 days	Tue 8/6/24
89	***Outdoor Pole Cameras (29)***	**5 days**	**Thu 8/8/24**
90	*Cable Installation*	3 days	Thu 8/8/24
91	*Camera Installation*	2 days	Tue 8/13/24
92	***Indoor& Outdoor cameras (12)***	**5 days**	**Thu 8/15/24**
93	*Cable Installation*	3 days	Thu 8/15/24
94	*Camera Installation*	2 days	Tue 8/20/24
95	*Inspections*	1 day	Tue 8/20/24
96	*Programming*	2 days	Tue 8/20/24
97	*Commissioning*	1 day	Thu 8/22/24
98	***Access Control Installation***	**8 days**	**Mon 9/16/24**
99	*Mobilization*	1 day	Mon 9/16/24
100	*Install Head End*	3 days	Tue 9/17/24
101	***Regular CR/Door (3)***	**2 days**	**Mon 9/23/24**
102	*Cable Installation*	1 day	Mon 9/23/24
103	*Device Installation*	1 day	Tue 9/24/24
104	***Biometrics CR/Door (2)***	**2 days**	**Tue 9/24/24**
105	*Cable Installation*	1 day	Tue 9/24/24
106	*Device Installation*	1 day	Wed 9/25/24
107	***Testing / Approvals***	**5 days**	**Thu 9/26/24**
108	*Final Contractor Testing*	1 day	Thu 9/26/24
109	*Final Contractor Punch List*	1 day	Fri 9/27/24
110	*Testing with the AHJ*	2 days	Mon 9/30/24
111	*Final Owner Sign Off*	1 day	Wed 10/2/24
112	***Close Out***	**3 days**	**Mon 9/30/24**

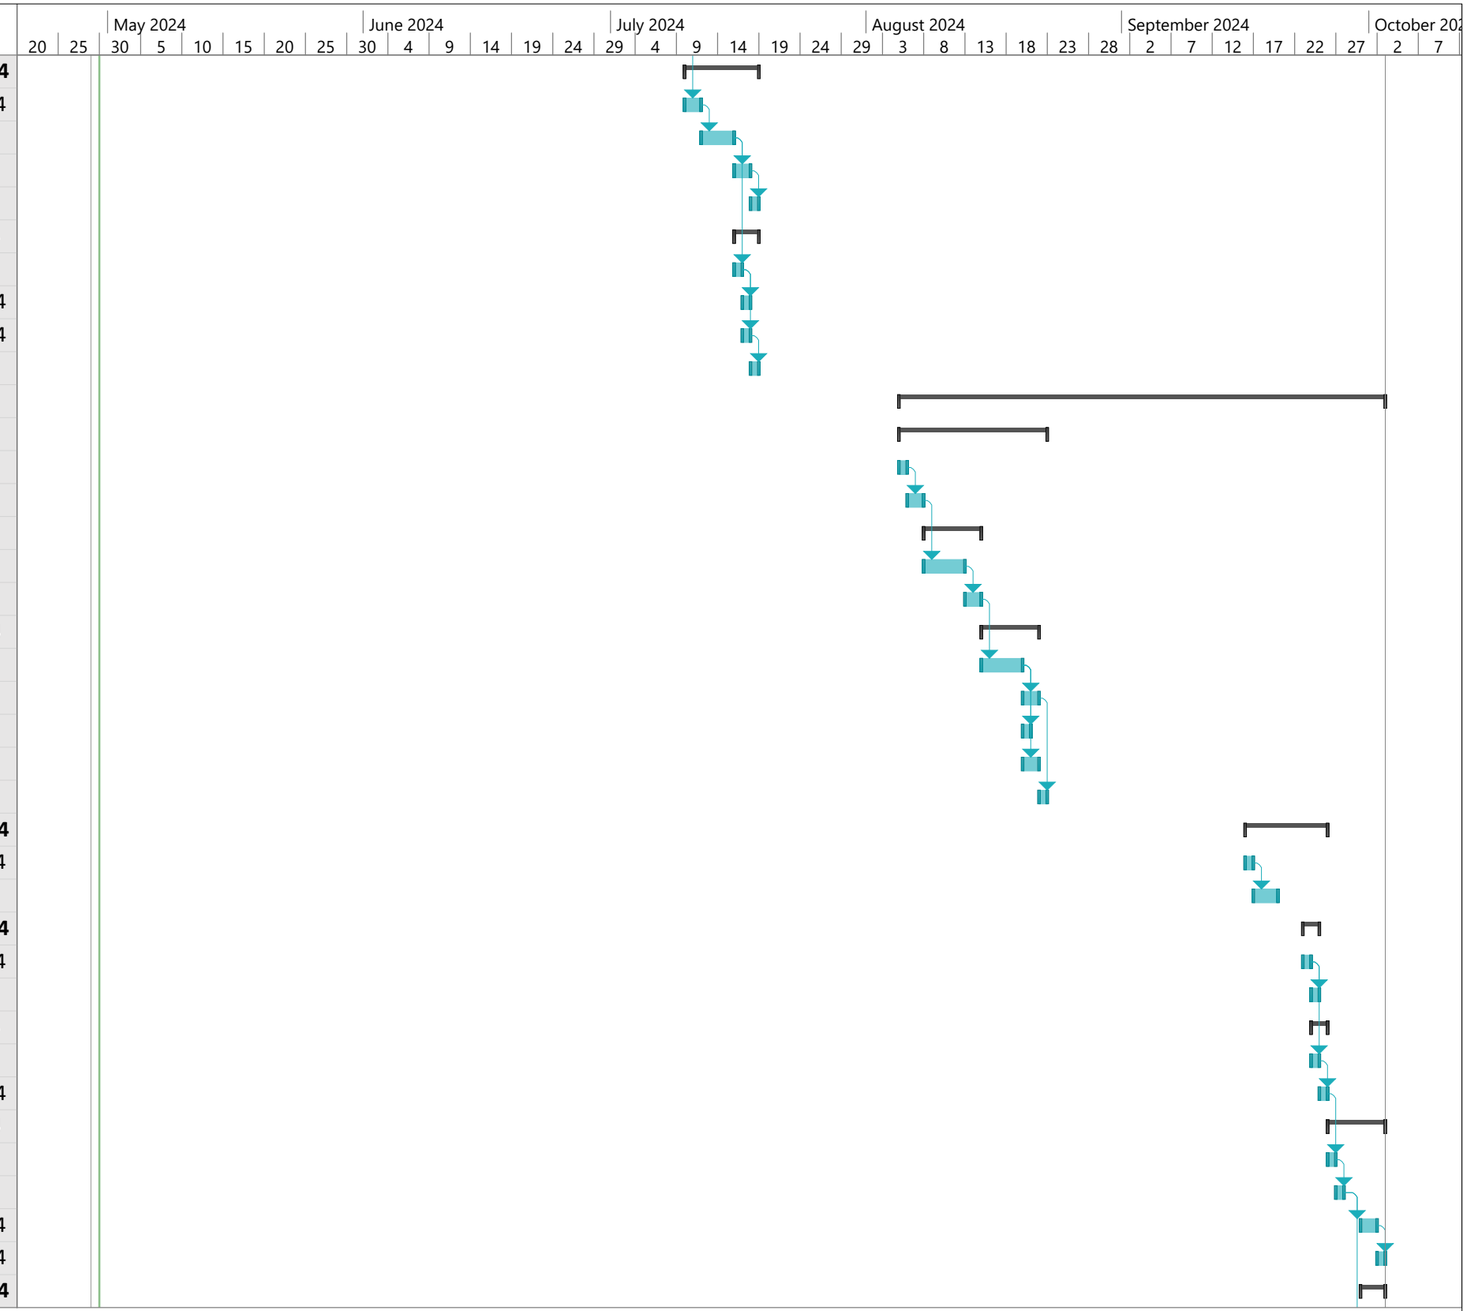

Project: City Of Doral CCTV & A
Date: Tue 4/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start
113	*As Built Drawings*	1 day	Mon 9/30/24
114	*O&M Manuals*	1 day	Tue 10/1/24
115	*Misc Close Out Submittals*	1 day	Tue 10/1/24
116	*Training*	1 day	Wed 10/2/24



Project: City Of Doral CCTV & A
Date: Tue 4/30/24

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
